



REPORTAGE TOWER

PROJECT MILESTONE
JULY 2026



JULY 2026




OZUMBA MBADIWE, VICTORIA ISLAND
LAGOS, NIGERIA

REPORTAGE TOWER

A structured roadmap outlining the key stages of development, with the preliminary phase successfully completed, the project is progressing toward subsequent phases.

PROJECT DEVELOPMENT PHASES 48 MONTHS TOTAL

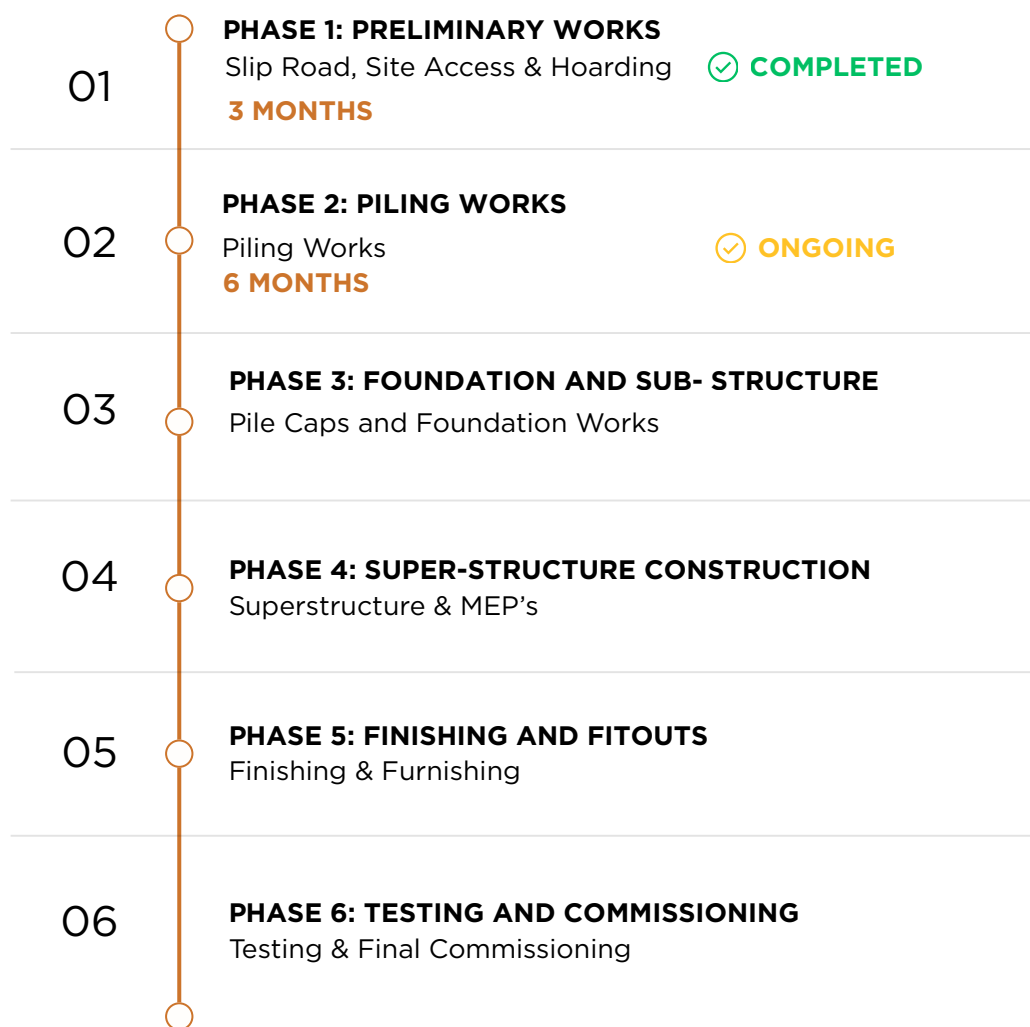

With the site now fully prepared and secured, the project has advanced into its next critical phase- **Piling Works**.

PHASE TWO ROADMAP

PILING WORKS

Building on a strong foundation, we have commenced piling works.

PHASE 2 ROADMAP- PILING WORKS (6 MONTHS)

SITE PREPARATION

COMPLETED

- ✓ Mobilization of Piling Contractor
- ✓ Site Handover and Possession
- ✓ Site Inspection and Logistics Planning
- ✓ Clearing of Trees, Shrubs and Vegetation
- ✓ Removal of Topsoil
- ✓ Demolition and Breaking of Existing Concrete Pavement/Slabs
- ✓ Earthworks and Ground Preparation
- ✓ Removal and Disposal of Demolition Debris
- ✓ Site Grading and Leveling
- ✓ Establishment of Temporary Access Routes for Heavy Equipment

PHASE 2 PROGRESS OVERVIEW



- ✓ COMPLETED
- ONGOING
- UPCOMING

SITE OFFICE AND WORKING AREA

COMPLETED

- ✓ Worker's Welfare Facilities
- ✓ Toilets and Changing Rooms
- ✓ Temporary Water Supply
- ✓ Temporary Electrical Power Distribution
- ✓ Site Lighting
- ✓ Internet and Communication Systems
- ✓ Construction of Piling Contractor's Site Offices
- ✓ Site Stores and Material Storage Area
- ✓ Workshop and Maintenance Area

QUALITY AND SAFETY SETUP

ONGOING

- Material Inspection Area
- Calibration of Surveying Equipment
- Calibration of Testing Equipment
- HSE Induction for all Personnel
- Emergency Response Procedures
- Fire Protection Equipment Installation
- First Aid Station Setup
- Environmental Protection Measures
- Traffic Management Plan Implementation

MAIN PILING EQUIPMENT

COMPLETED

- ✓ Mobilization of Cranes
- ✓ Mobilization of Excavators
- ✓ Mobilization of Piling Rig
- ✓ Mobilization of Dump Trucks
- ✓ Mobilization of Bentonite Mixing Plant
- ✓ Installation of Bentonite Storage Tanks
- ✓ Generator Installation

SURVEY AND SETTING OUT

COMPLETED

- ✓ Establish Project Control Points
- ✓ Survey Benchmark Verification
- ✓ Pile Grid Setting Out
- ✓ Pile Position Marking
- ✓ Survey Validation and Approval

GENERAL PILING WORKS

UPCOMING

- Dilapidation Survey of Eko Court
- Drilling of Trial/Test Pile
- Testing of Trial Pile
- Drilling and Installation of Bored Piles
- Drilling and Installation of Secant Piles
- Concrete Washout Area

Thank you

Thank you for your continued trust and confidence in the progress of Reportage Tower.

We look forward to sharing the next phase of development with you.

